

Panther Grove 2

	6-Oct-26	Today
Daily Weather as of 7:00am	Sunny	Sunny
Low Temperature (F)	55	51
High Temperature (F)	77	82
Ground Wind Speed (MPH):	3 MPH	10 MPH
Precipitation (in)	0.00	2%
September Precip Total (in)	1.00	

	ACTIVITY
Public Roads	Strip Public Road Radii
	Mowing Public Road Radii
	Stone Public Road Radii
Access Roads	Strip Access Road
	Cement Stabilization
	Stone Access Road
	Strip Access Road Radii
	Stone Access Road Radii

LAST WORKING DAY
Tuesday, October 6, 2026
LOCATION(S)
P8
No Work Due to Access / Permit Restrictions
No Work Due to Access / Permit Restrictions
T92, T86
No Work Due to Access / Permit Restrictions
No Work Due to Access / Permit Restrictions
No Work Due to Access / Permit Restrictions
No Work Due to Access / Permit Restrictions
No Work Due to Access / Permit Restrictions

Daily Safety Topics
Stop the Drop Campaign- Recognize the exposure and secure the object.
-Perform a Team Check and find three dropped-object exposures and correct them. Document on SSC & SPO
-Inspect tools, attachment points, bags, containers, and secondary retention
Site Notes

Wednesday, October 7, 2026

TODAY
Wednesday, October 7, 2026
LOCATION(S)
P8
No Work Due to Access / Permit Restrictions
P8
T86
No Work Due to Access / Permit Restrictions
No Work Due to Access / Permit Restrictions
T88
T88


NEXT WORKING DAY
Thursday, October 8, 2026
LOCATION(S)
P8
No Work Due to Access / Permit Restrictions
P8
T81
No Work Due to Access / Permit Restrictions
No Work Due to Access / Permit Restrictions
T88
T88



Quantity Tracking				
QTY LAST WORKDAY	QTY TO DATE	UNIT	TOTAL QTY	% COMPLETE
	9	EA	35	25.7%
	8	EA	35	22.9%
1	49162	LF	161120	30.5%
	47329.5	LF	161120	29.4%
	38204	LF	161120	23.7%
	36	EA	TBD	#VALUE!
	29	EA	TBD	#VALUE!

Site Information	
Manpower	
10	White Construction Management
33	White Construction Operators
25	White Construction Laborers
14	White Construction Ironworkers
0	White Construction Millwright
2	White Construction Electrician
40	Dunn Company
8	West Wind
4	Tobey's Construction & Cartage
8	KVCC
6	Prairie Materials
150	Total
Equipment	
37	Pickup Trucks
3	Dozers
0	Rollers
1	Graders
0	Cargo Trailer
0	Cranes
3	Excavators
0	Forklift
16	Trailers
0	Sand Truck
1	Sheepfoot Roller
0	Reclaimer Stabilizer
2	Smooth Drum Roller
2	Water Trucks
7	Skid Steer
72	Total

Additional Comments

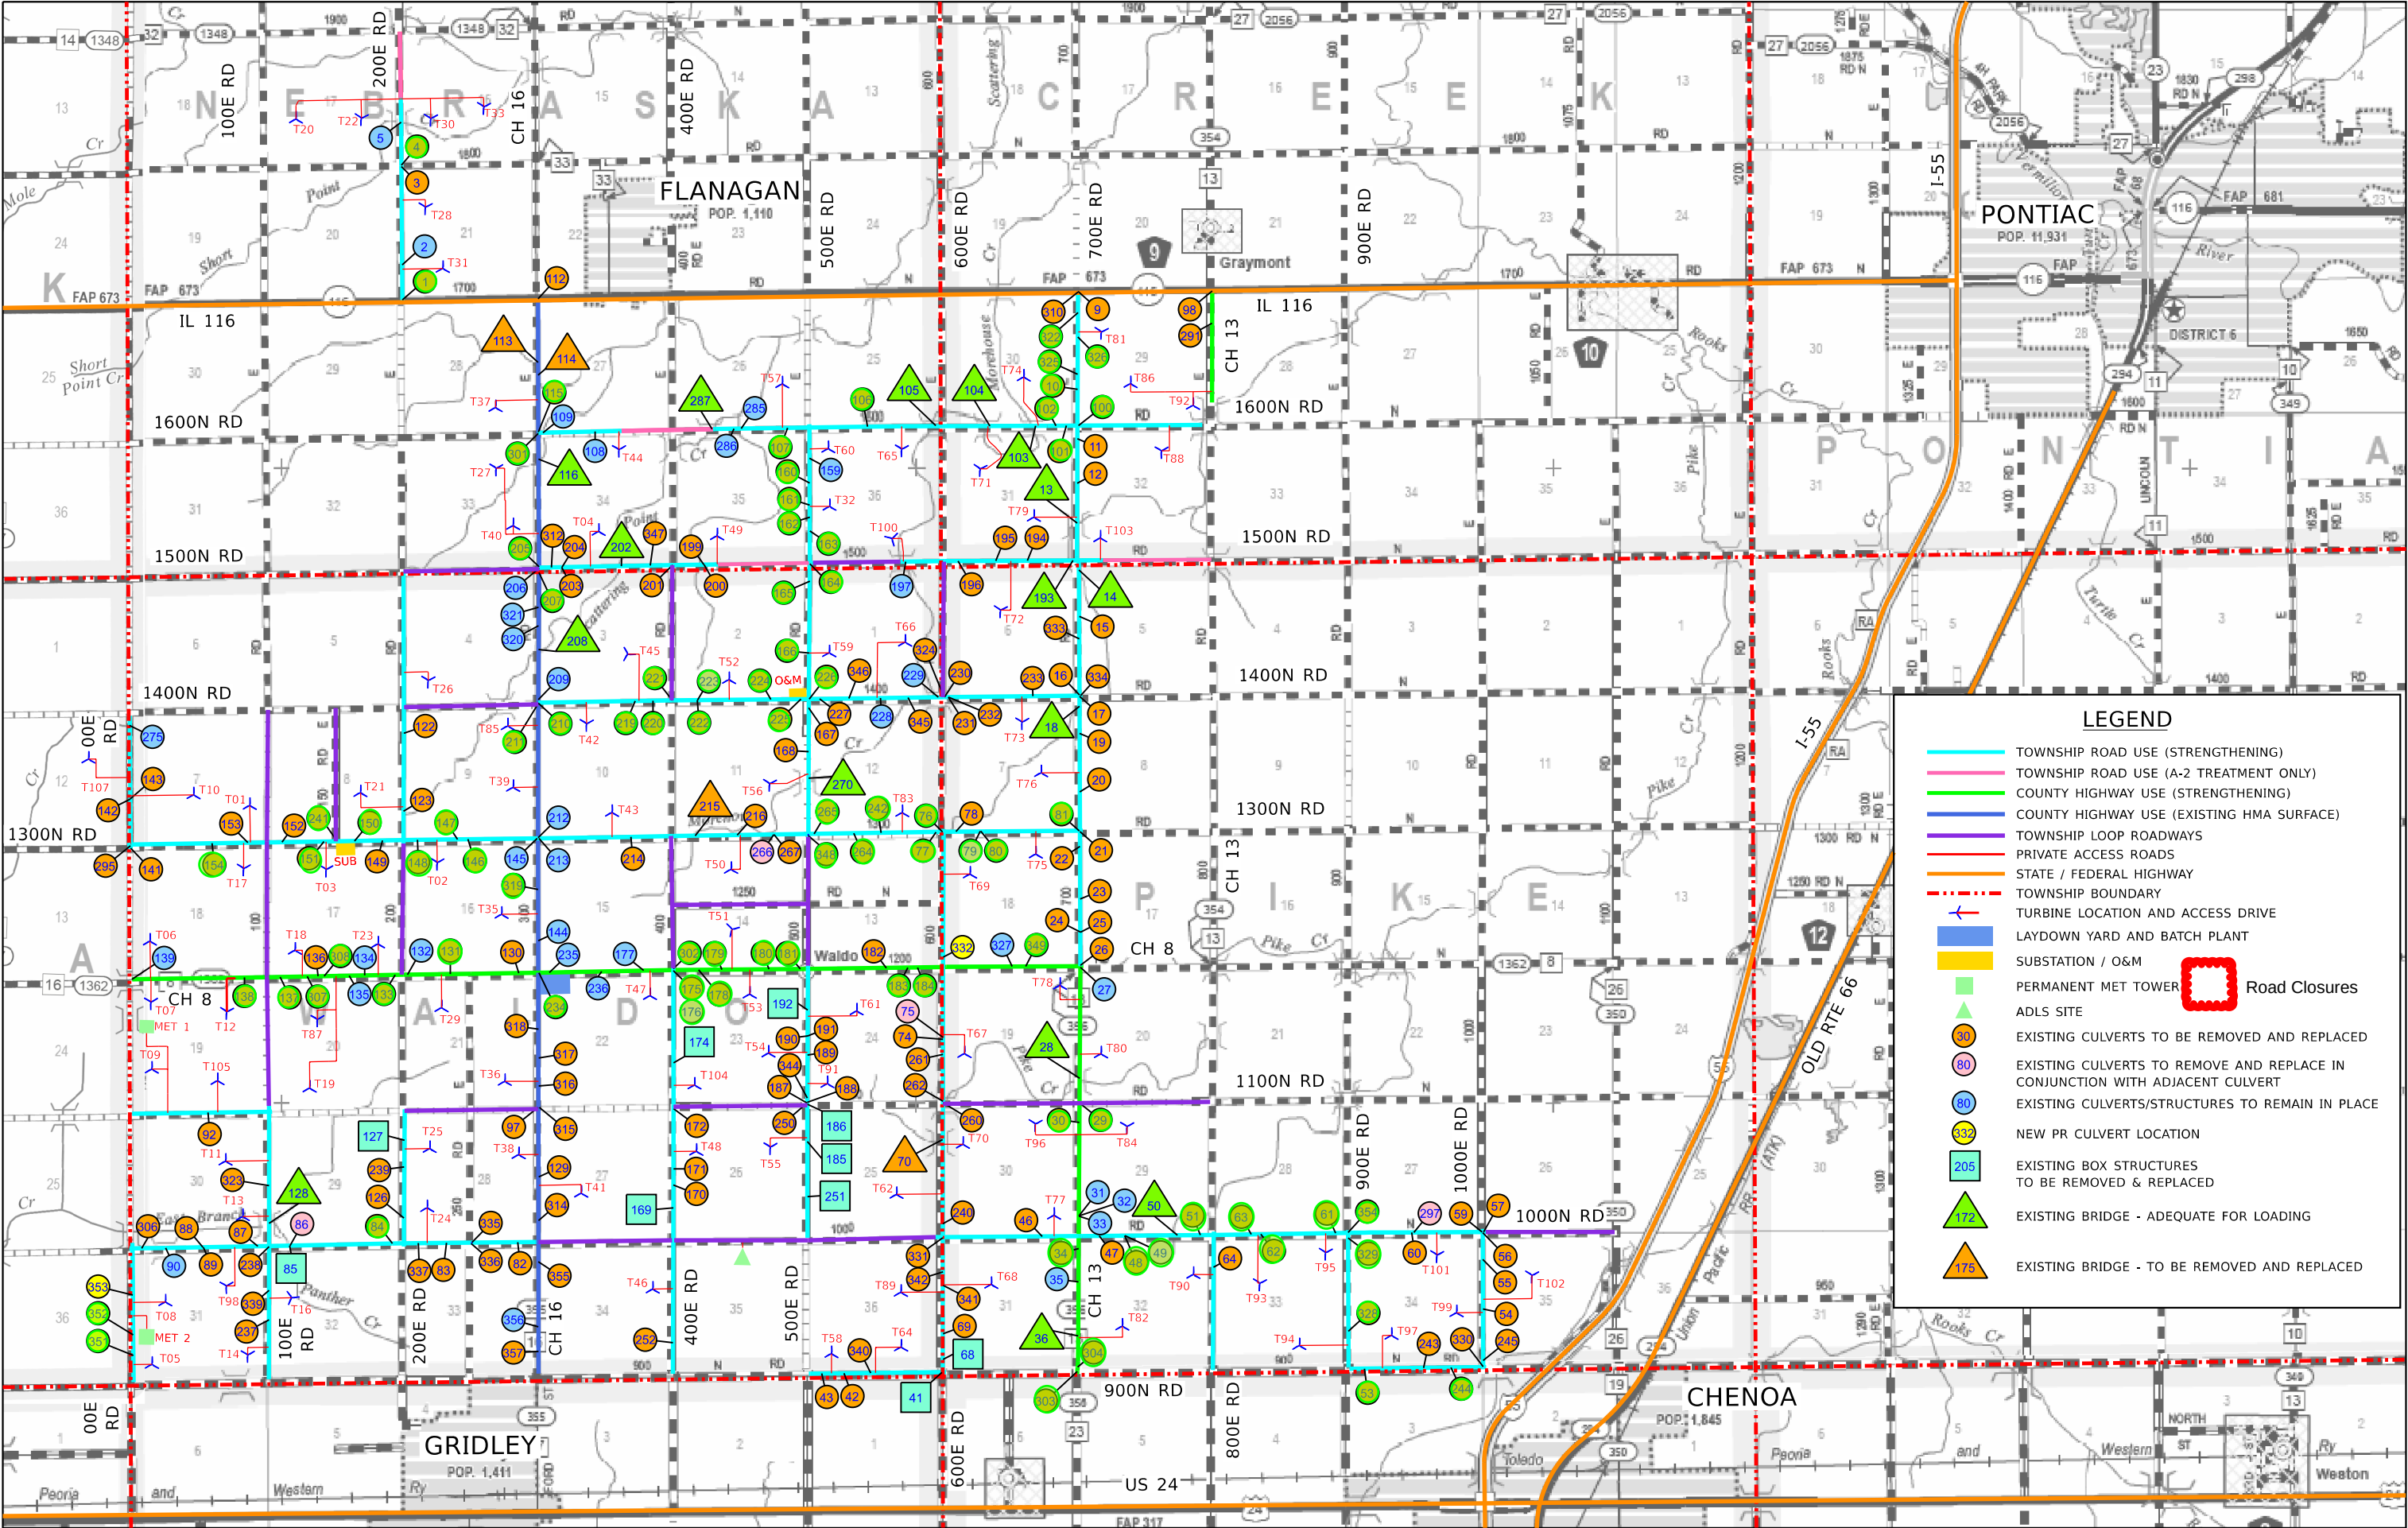

LEGEND

TOWNSHIP ROAD USE (STRENGTHENING)

TOWNSHIP ROAD USE (A-2 TREATMENT ONLY)

COUNTY HIGHWAY USE (STRENGTHENING)

COUNTY HIGHWAY USE (EXISTING HMA SURFACE)

TOWNSHIP LOOP ROADWAYS

PRIVATE ACCESS ROADS

STATE / FEDERAL HIGHWAY

TOWNSHIP BOUNDARY

TURBINE LOCATION AND ACCESS DRIVE

LAYDOWN YARD AND BATCH PLANT

SUBSTATION / O&M

PERMANENT MET TOWER

ADLS SITE

EXISTING CULVERTS TO BE REMOVED AND REPLACED

EXISTING CULVERTS TO REMOVE AND REPLACE IN CONJUNCTION WITH ADJACENT CULVERT

EXISTING CULVERTS/STRUCTURES TO REMAIN IN PLACE

NEW PR CULVERT LOCATION

EXISTING BOX STRUCTURES TO BE REMOVED & REPLACED

EXISTING BRIDGE - ADEQUATE FOR LOADING

EXISTING BRIDGE - TO BE REMOVED AND REPLACED

Road Closures

