Plan of the Day (POD) Report

20-Nov-2026

PANTHER GROVE WIND ENERGY FACILITY

Weather Notes: Rain out on 10-15				
	66° / 43° Temp Range	66° / 42° Temp Range	64° / 49° Temp Range	59° / 38° Temp Range
	None Precipitation	None Precipitation	12% | 0.00 in | None Precipitation	46% | 0.13 in | 1 AM - 6 PM Precipitation
	None | None Lighting Risk	None | None Lighting Risk	None | None Lighting Risk	None | None Lighting Risk
	None | 0% | None Severe Forcast	None | 0% | None Severe Forcast	None | 0% | None Severe Forcast	None | 0% | None Severe Forcast
	17.2 Max Wind	13.2 Max Wind	16.1 Max Wind	17.7 Max Wind
	30 Max Gust	33.3 Max Gust	32.2 Max Gust	28.2 Max Gust

(S) Start
(C) Continue
(F) Finish

LAST WORKING DAY	TODAY	NEXT WORKING DAY	2-Day Lookahead
Thursday, November 19, 2026	Friday, November 20, 2026	Saturday, November 21, 2026	Sunday, November 22, 2026

Today's Notes

Active Cure	Date	Day	Cure		
CH8:CH16-400E	10/23	28	10/30		
N/A					
N/A					
N/A					
N/A					

Manpower	Scope	QTY
Dunn Company	Punchlish	6
Tobey's Constr.	Pipe Culvert	6
KVCC	HMA	4
Millennia	QC	0
Material Serv. Test.	QC	0
Beniach	Oil and Chip	0

Notes:
Box Culvert: In procurement

Pipe Culvert: Ongoing

Agg Widening: On hold

Profile Adj./Add Rock: On hold

Pulverization: on hold

Stabilization: on hold

Agg Surface: on hold

Oil and Chip: on hold

Earthwork: on hold

Seeding: on hold

HMA: On hold until IDOT permits are in place.

Punchlist: On going

	LOCATION(S) Road	Repening	LOCATION(S) Road	Repening	LOCATION(S) Road	Repening	LOCATION(S) Road	Repening
Long Duration Road Closures								
Short Duration Road Closures	☑ 1000N:00E-100E	11/19/2026	☑ 1000N:00E-100E	11/19/2026				
	☐ 00E:1300N-1400N	11/23/2026	☐ 00E:1300N-1400N	11/23/2026	☐ 00E:1300N-1400N	11/23/2026	☐ 00E:1300N-1400N	11/23/2026
	☐ 00E-CH8-1300N	11/23/2026	☐ 00E-CH8-1300N	11/23/2026	☐ 00E-CH8-1300N	11/23/2026	☐ 00E-CH8-1300N	11/23/2026
	☐ 700E:CH8-1300N	11/23/2026	☐ 700E:CH8-1300N	11/23/2026	☐ 700E:CH8-1300N	11/23/2026		

			QTY Last Work Day	QTY Complete	Unit	Total QTY	% Complete			
Public Road Improvements	Box Culvert		0.0	1.0	EA	15.0	6.7%			
	Pipe Culvert	C 26 C 143 C 142 C 141	0.0	117.0	EA	222.0	52.7%	C 26 Backfill C 143 C 142 C 141	C 143 Strip Forms C 142 Strip Forms C 141	
	Aggregate Widening		0.0	23.0	Mi	75.0	30.7%			
	Prof. Adj.		0.0	12.0	EA					
	Pulverization		0.0	23.5	Mi	75.0	31.3%			
	Stabilization		0.0	23.5	Mi	75.0	31.3%			
	Agg Surface		0.0	23.5	Mi	75.0	31.3%			
	Oil and Chip		0.0	23.5	Mi	75.0	31.3%			
	Earthwork		0.0	23.5	Mi	75.0	31.3%			
	Seeding		0.0	23.5	Mi	75.0	31.3%			
	Punchlist		0.0	23.5	Mi	75.0	31.3%			
	HMA		0.0	7.0	EA	17.0	41.2%			
	Maintenance									
	M120 Cold Patch Install	F Field Tile @ culvert 90	0.0	0.0	EA	17.0		S Field Tile @ culvert 90		
Site	Crane Pad		0.0	15.0	EA	109.0	13.8%			
	Access Road		0.0	43.0	EA	109.0	39.4%			

Panther Grove 2

	19-Nov-26	Today
Daily Weather as of 7:00am	Clear	Clear
Low Temperature (F)	29	35
High Temperature (F)	57	61
Ground Wind Speed (MPH):	9	13
Precipitation (in)	0.00	6%
November Precip Total (In)	0.80	

Daily Safety Topics

Signing into a work area: When we visit a job area let's make sure to take the time to review JSA and sign in to the log. This applies to everyone at every level from Supervision, craft, client, inspectors, PM's, APM's' FE's an, etc.. If you are stepping into someone's work area you have an obligation to sign in regardless of the time spent in the area.
Housekeeping and Material Control: Keep work areas free of trip hazards. Secure tools and materials to prevent dropped objects. Maintain clear access and egress routes.

Site Notes

Friday, November 20, 2026

	ACTIVITY	LAST WORKING DAY Thursday, November 19, 2026 LOCATION(S)	TODAY Friday, November 20, 2026 LOCATION(S)	NEXT WORKING DAY Saturday, November 21, 2026 LOCATION(S)
Public Roads	Strip Public Road Radii	P16 (1300N RD / 200E RD)		
	Mowing Public Road Radii			
	Stone Public Road Radii	P32 (1000N RD / CH 13 -- NW),	P32 (1000N RD / CH 13 -- NW), P16 (1300N RD / 200E RD)	P32 (1000N RD / CH 13 -- NW), P16 (1300N RD / 200E RD)
Access Roads	Strip Access Road	T09, MET Tower		
	Cement Stabilization			
	Stone Access Road			
	Strip Access Road Radii			
	Stone Access Road Radii	T59, T53, T51	T53, T41, T47	

Quantity Tracking

QTY LAST WORKDAY	QTY TO DATE	UNIT	TOTAL QTY	% COMPLETE
	11	EA	35	31.4%
	11	EA	35	31.4%
	78138	LF	161120	48.5%
	79270.5	LF	161120	49.2%
	61659.5	LF	161120	38.3%
	64	EA	140	45.7%
	61	EA	140	43.6%

Site Information


Manpower

19	White Construction Management
47	White Construction Operators
27	White Construction Laborers
16	White Construction Ironworkers
0	White Construction Millwright
3	White Construction Electrician
15	Dunn Company
8	West Wind
0	Tobey's Construction & Cartage
0	KVCC
6	Prairie Materials
19	JF Edwards
5	Keeley
165	**Total**

Equipment

48	Pickup Trucks
3	Dozers
0	Rollers
1	Graders
1	Cargo Trailer
0	Cranes
3	Excavators
0	Forklift
13	Trailers
0	Sand Truck
1	Sheepfoot Roller
0	Reclaimer Stabilizer
1	Smooth Drum Roller
2	Water Trucks
5	Skid Steer
78	**Total**

Additional Comments

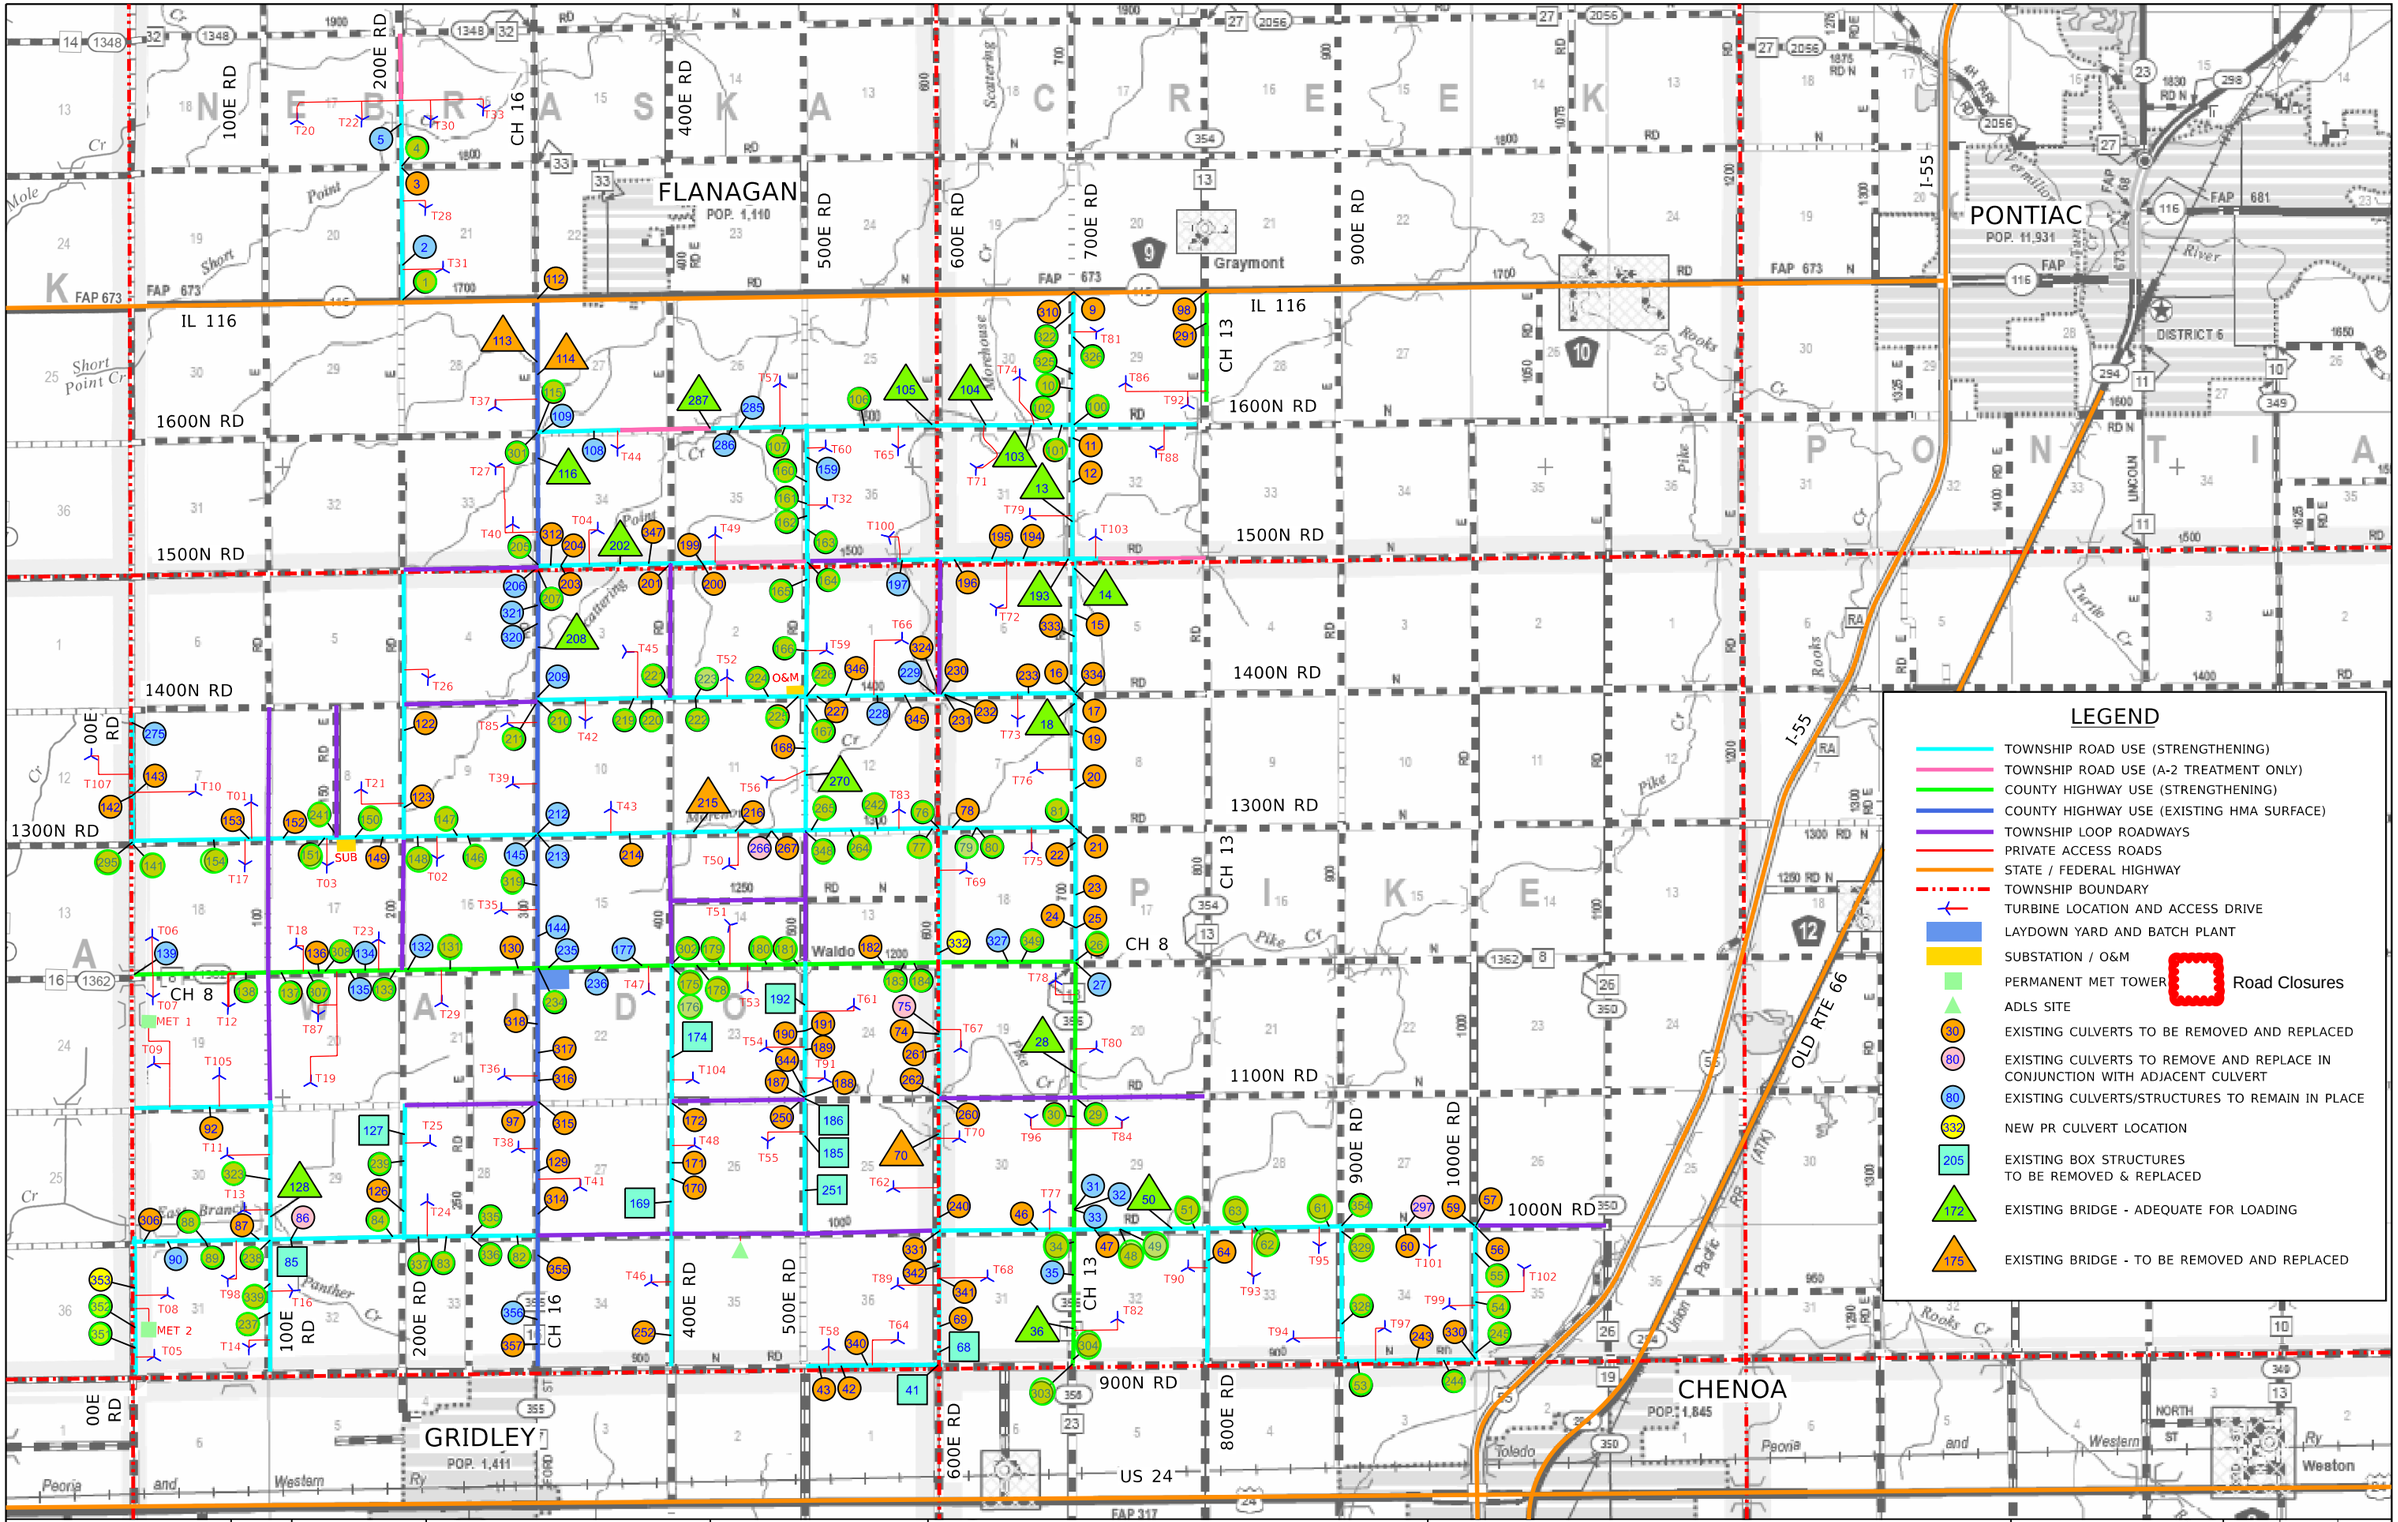

REV	DATE	DESCRIPTION
1	4/10/2026	REV 1
00	2/20/2026	IFC SUBMITTAL

DESIGNED - JDA
DRAWN - DRR/LNS
CHECKED - ML
DATE - 04/14/2026

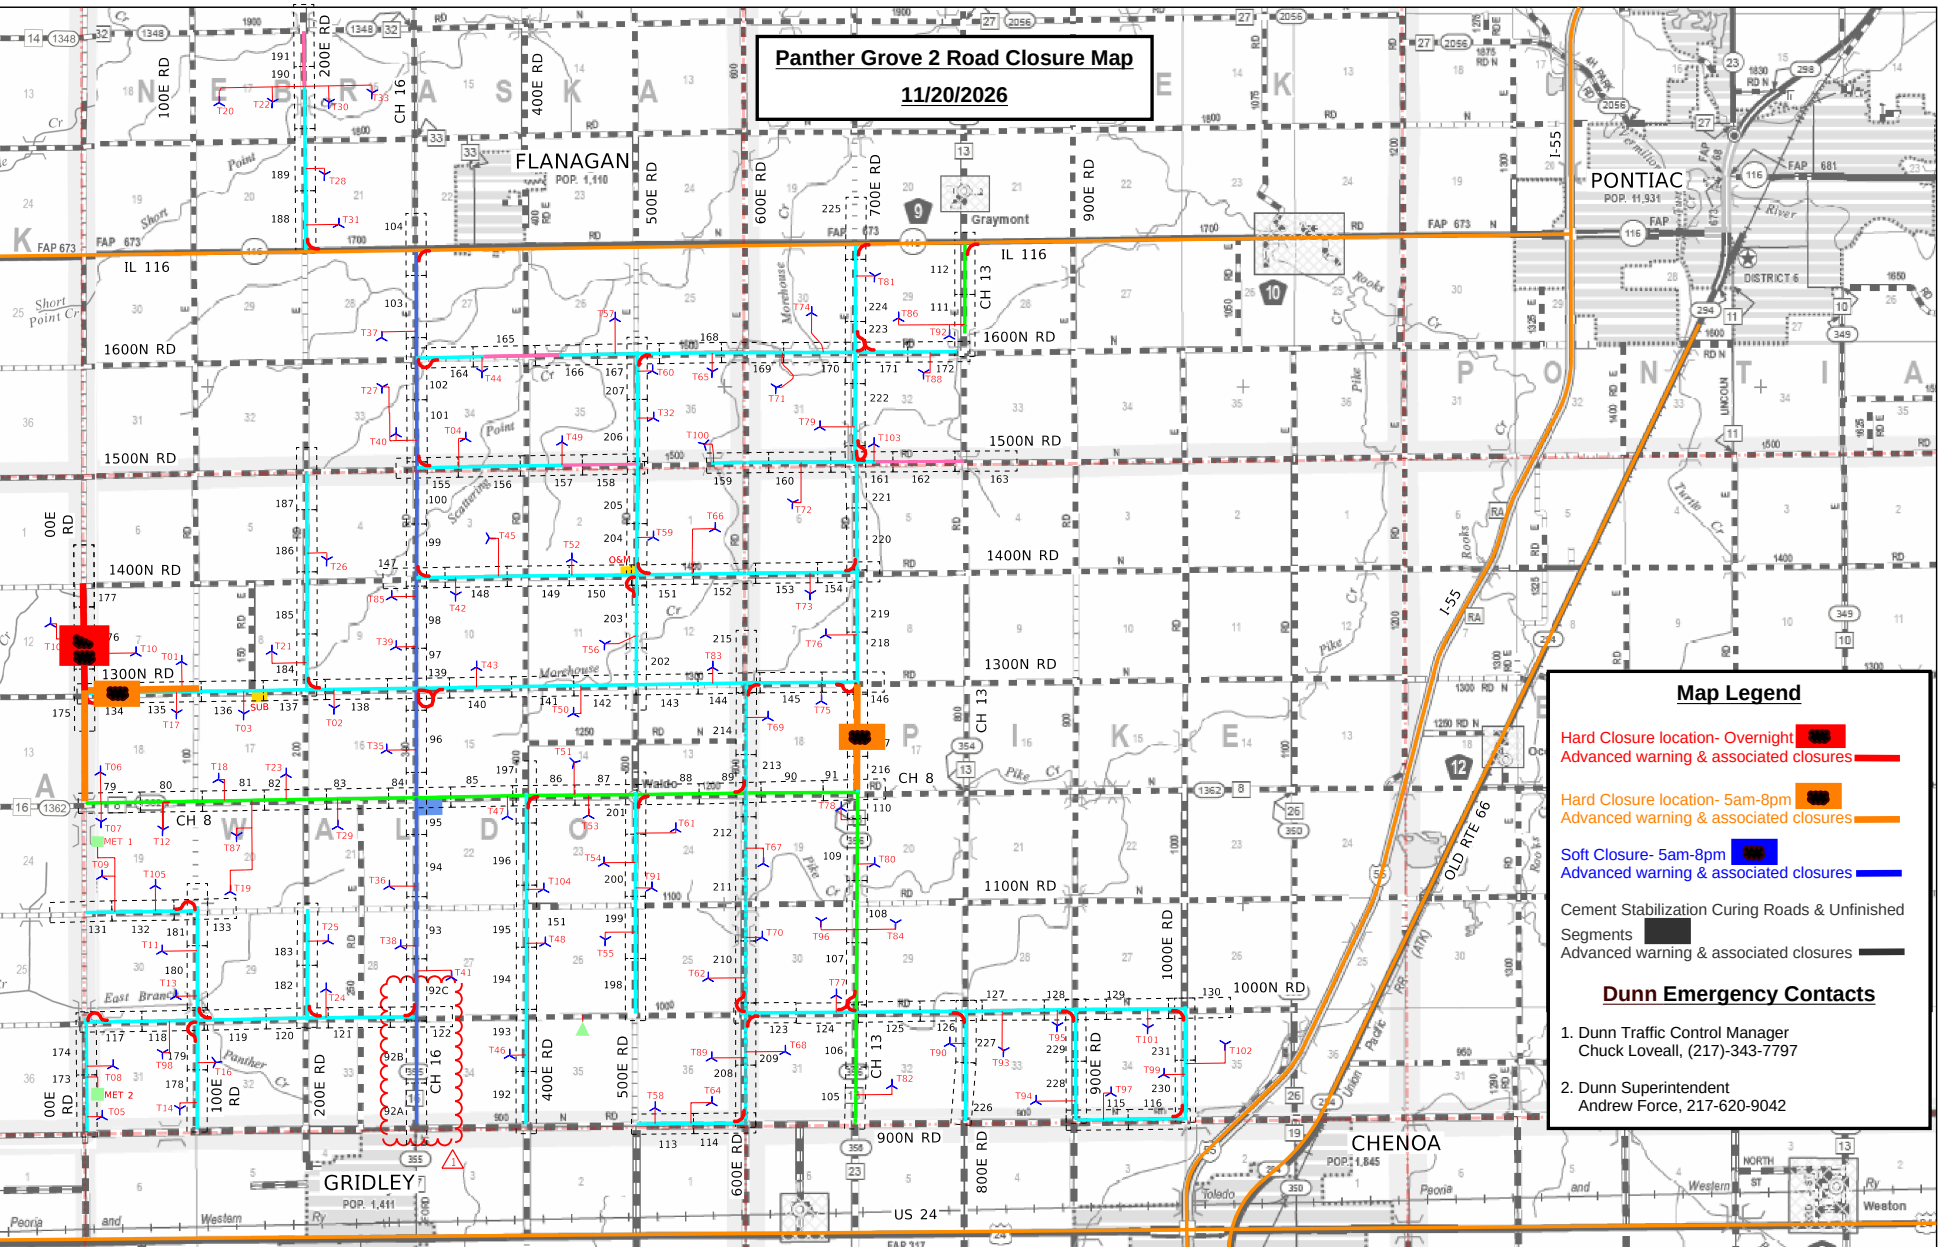
PANTHER GROVE 2 WIND PROJECT
LIVINGSTON COUNTY, ILLINOIS

EXHIBIT A – PROJECT LAYOUT MAP (REVISION 1)

SCALE: N.T.S. | SHEET 1 OF 1 SHEETS | STA. | TO STA.

Farnsworth GROUP
100 WALNUT ST #200
PEORIA, ILLINOIS 61602
(309) 689-9888 / Info@f-w.com

TOTAL SHEETS	SHEET NO.	REVISION NO.


Panther Grove 2 Road Closure Map
11/20/2026
Map Legend
Hard Closure location- Overnight
Advanced warning & associated closures
Hard Closure location- 5am-8pm
Advanced warning & associated closures
Soft Closure- 5am-8pm
Advanced warning & associated closures
Cement Stabilization Curing Roads & Unfinished Segments
Advanced warning & associated closures
Dunn Emergency Contacts
1. Dunn Traffic Control Manager
Chuck Loveall, (217)-343-7797
2. Dunn Superintendent
Andrew Force, 217-620-9042
FLANAGAN
POP. 1,110
PONTIAC
POP. 11,931
GRIDLEY
POP. 1,411
CHENOA
POP. 1,845
IL 116
1600N RD
1500N RD
1400N RD
1300N RD
1100N RD
1000N RD
900N RD
US 24
CH 8
CH 13
CH 16
100E RD
200E RD
400E RD
500E RD
600E RD
700E RD
800E RD
900E RD
1000E RD
I-55
OLD RTE 66
Graymont
DISTRICT 6
Waldo
Pike Cr
Panther Cr
Short Point Cr
Scattering Point
Morehouse
Rooks Cr
Turtle Cr
Peoria and Western Ry
Toledo Peoria and Western Ry
Union Pacific (ATK)
