Panther Grove 2

	20-Nov-26	Today
Daily Weather as of 7:00am	Sunny	Sunny
Low Temperature (F)	45	46
High Temperature (F)	63	71
Ground Wind Speed (MPH):	15 mph	13 mph
Precipitation (in)	0.0	3%
November Precip Total (In)	1.0	

Daily Safety Topics

Visitors on Job Site: Visitors are not part of the active construction crew and may not recognize changing jobsite hazards. Protect visitors by keeping them out of work zones unless they are authorized, briefed, and escorted as required.

Communication - Make sure there is good communication between different crews when working within the same area. Ensure you know what task they are completing with their hazards, and they are aware of yours.

Site Notes

Saturday, November 21, 2026

	ACTIVITY	LAST WORKING DAY Friday, November 20, 2026 LOCATION(S)	TODAY Saturday, November 21, 2026 LOCATION(S)	NEXT WORKING DAY Monday, November 23, 2026 LOCATION(S)	QTY LAST WORKDAY	QTY TO DATE	UNIT	TOTAL QTY	% COMPLETE
Misc	Misc.								
Public Roads	Strip Public Road Radii	P32 (1000N RD / CH 13 -- NW) P16 (1300N RD / 200E RD)	P32 (1000N RD / CH 13 -- NW) P16 (1300N RD / 200E RD)	P32 (1000N RD / CH 13 -- NW) P16 (1300N RD / 200E RD)		15	EA	35	42.9%
	Mowing								
	Stone Public Road Radii	P32 (1000N RD / CH 13 -- NW) P16 (1300N RD / 200E RD)	P32 (1000N RD / CH 13 -- NW) P16 (1300N RD / 200E RD)	P32 (1000N RD / CH 13 -- NW) P16 (1300N RD / 200E RD)		13	EA	35	37.1%
Access Roads	Strip Access Road					80468	LF	161120	49.9%
	Cement Stabilization	T09, MET Tower		T09, MET Tower		79270.5	LF	161120	49.2%
	Stone Access Road					65954.5	LF	161120	40.9%
	Strip Access Road Radii					64	EA	140	45.7%
	Stone Access Road Radii	T47, T51, T53		T47, T51, T53		61	EA	140	43.6%
Foundations	Strip Sites	T09, T77		T09, T77		53	EA	105	50.5%
	Geo-Piers					6	EA	14	42.9%
	Excavate Foundations	T96		T84	1	46	EA	105	43.8%
	Mud Mat	T78		T80, T96, T84	1	45	EA	105	42.9%
	Rebar Delivery	T71		T65	1	33	EA	105	31.4%
	Rebar Bottom Mat	T71		T65	1	33	EA	105	31.4%
	Anchor Bolt Build	T02		T03	1	41	EA	105	39.0%
	Anchor Bolt Set	T71		T65	1	33	EA	105	31.4%
	Rebar Top Mat	T71,T86		T71,T65	1	32	EA	105	30.5%
	Pour Base	T92	T86	T74	1	30	EA	105	28.6%
	Rebar Pedestal	T88		T92	1	29	EA	105	27.6%
	Form Pedestal	T88		T92	1	29	EA	105	27.6%
	Pour Pedestal	T81	T88	T92	1	28	EA	105	26.7%
	Strip Pedestal	T51, T53		T81	1	27	EA	105	25.7%
	Backfill Foundation	T51, T53	T53	T53, T81	1	26	EA	105	24.8%
	Crane Pad Subgrade	T51, T53	T53	T53, T81	1	23	EA	105	21.9%
	Crane Pad Stabilization					18	EA	105	17.1%
	Crane Pad Stone					7	EA	105	6.7%
	Set Load Spreader Plate					0	EA	105	0.0%
	Set Grout Forms					0	EA	105	0.0%

Quantity Tracking

Site Information

Manpower

18	White Construction Management
45	White Construction Operators
25	White Construction Laborers
17	White Construction Ironworkers
0	White Construction Millwright
3	White Construction Electrician
15	Dunn Company
8	West Wind
0	Tobey Construction & Cartage
0	KVCC
6	Prairie Materials
19	JF Edwards
19	JF Edwards
5	Keeley
180	**Total**

Equipment

48	Pickup Trucks
3	Dozers
5	Skid Steers
0	Rollers
1	Graders
1	Cargo Trailers
0	Reclaimer Stabilizer
3	Excavators
1	Smooth Drum Roller
13	Trailers
2	Water Trucks
1	Sheepfoot roller
78	**Total**

Qty Executed	Completion Certificates
0/20	WTG Civil Works Completion
0/105	WTG Foundation Completion
0/105	WTG Mechanical Completion
0/20	Collection Circuit Mechanical Completion
0/1	Substation Mechanical Completion
0/1	Electrical Substantial Completion
0/1	O&M Building Substantial Completion
0/1	Final Completion

Plan of the Day (POD) Report

21-Nov-2026

PANTHER GROVE WIND ENERGY FACILITY

Weather Notes: Rain out on 10-15	LAST WORKING DAY	TODAY	NEXT WORKING DAY	2-Day Lookahead
	69° / 39° Temp Range	69° / 44° Temp Range	56° / 39° Temp Range	45° / 33° Temp Range
	None Precipitation	None Precipitation	72% | 0.09 in | 7 AM - 6 PM Precipitation	10% | 0.00 in | None Precipitation
	None | None Lighting Risk	None | None Lighting Risk	None | None Lighting Risk	None | None Lighting Risk
	None | 0% | None Severe Forcast	None | 0% | None Severe Forcast	None | 0% | None Severe Forcast	None | 0% | None Severe Forcast
	14.6 Max Wind	14.3 Max Wind	15.4 Max Wind	10 Max Wind
	23.7 Max Gust	25.1 Max Gust	33.3 Max Gust	23.3 Max Gust
(S) Start (C) Continue (F) Finish	Friday, November 20, 2026	Saturday, November 21, 2026	Sunday, November 22, 2026	Monday, November 23, 2026
	LOCATION(S) Road / Repening	LOCATION(S) Road / Repening	LOCATION(S) Road / Repening	LOCATION(S) Road / Repening

Today's Notes

Active Cure	Date	Day	Cure		
CH8:CH16-400E	10/23	29	10/30		
N/A					
N/A					
N/A					
N/A					

Manpower	Scope	QTY
Dunn Company	Punchlish	6
Tobey's Constr.	Pipe Culvert	6
KVCC	HMA	4
Millennia	QC	0
Material Serv. Test.	QC	0
Beniach	Oil and Chip	0

Notes:

Box Culvert: In procurement

Pipe Culvert: Ongoing

Agg Widening: On hold

Profile Adj./Add Rock: On hold

Pulverization: on hold

Stabilization: on hold

Agg Surface: on hold

Oil and Chip: on hold

Earthwork: on hold

Seeding: on hold

HMA: On hold until IDOT permits are in place.

Punchlist: On going


Long Duration Road Closures

Short Duration Road Closures

	LAST WORKING DAY	TODAY	NEXT WORKING DAY	2-Day Lookahead
Long Duration Road Closures				
Short Duration Road Closures	☑ 1000N:00E-100E 11/19/2026 ☐ 00E:1300N-1400N 11/23/2026 ☐ 00E-CH8-1300N 11/23/2026 ☐ 700E:CH8-1300N 11/23/2026	☐ 00E:1300N-1400N 11/23/2026	☐ 00E:1300N-1400N 11/23/2026	☐ 00E:1300N-1400N 11/23/2026 ☐ 00E-CH8-1300N 11/23/2026 ☐ 700E:CH8-1300N 11/23/2026

		QTY Last Work Day	QTY Complete	Unit	Total QTY	% Complete	TODAY	NEXT WORKING DAY	2-Day Lookahead
Public Road Improvements	Box Culvert	0.0	1.0	EA	15.0	6.7%			
	Pipe Culvert	1.0	118.0	EA	222.0	53.2%	C 143 Strip Forms C 142 Strip Forms		C 26 Closeout C 143 Place Pipe C 142 Place Pipe C 141
	Aggregate Widening	0.0	23.0	Mi	75.0	30.7%			
	Prof. Adj.	0.0	12.0	EA					
	Pulverization	0.0	23.5	Mi	75.0	31.3%			
	Stabilization	0.0	23.5	Mi	75.0	31.3%			
	Agg Surface	0.0	23.5	Mi	75.0	31.3%			
	Oil and Chip	0.0	23.5	Mi	75.0	31.3%			
	Earthwork	0.0	23.5	Mi	75.0	31.3%			
	Seeding	0.0	23.5	Mi	75.0	31.3%			
	Punchlist	0.0	23.5	Mi	75.0	31.3%			
	HMA	0.0	7.0	EA	17.0	41.2%			
	Maintenance								
	M120 Cold Patch Install	0.0	0.0	EA	17.0				
Site	Crane Pad	0.0	15.0	EA	109.0	13.8%			
	Access Road	0.0	43.0	EA	109.0	39.4%			

F 26 Backfill
C 143
C 142
C 141

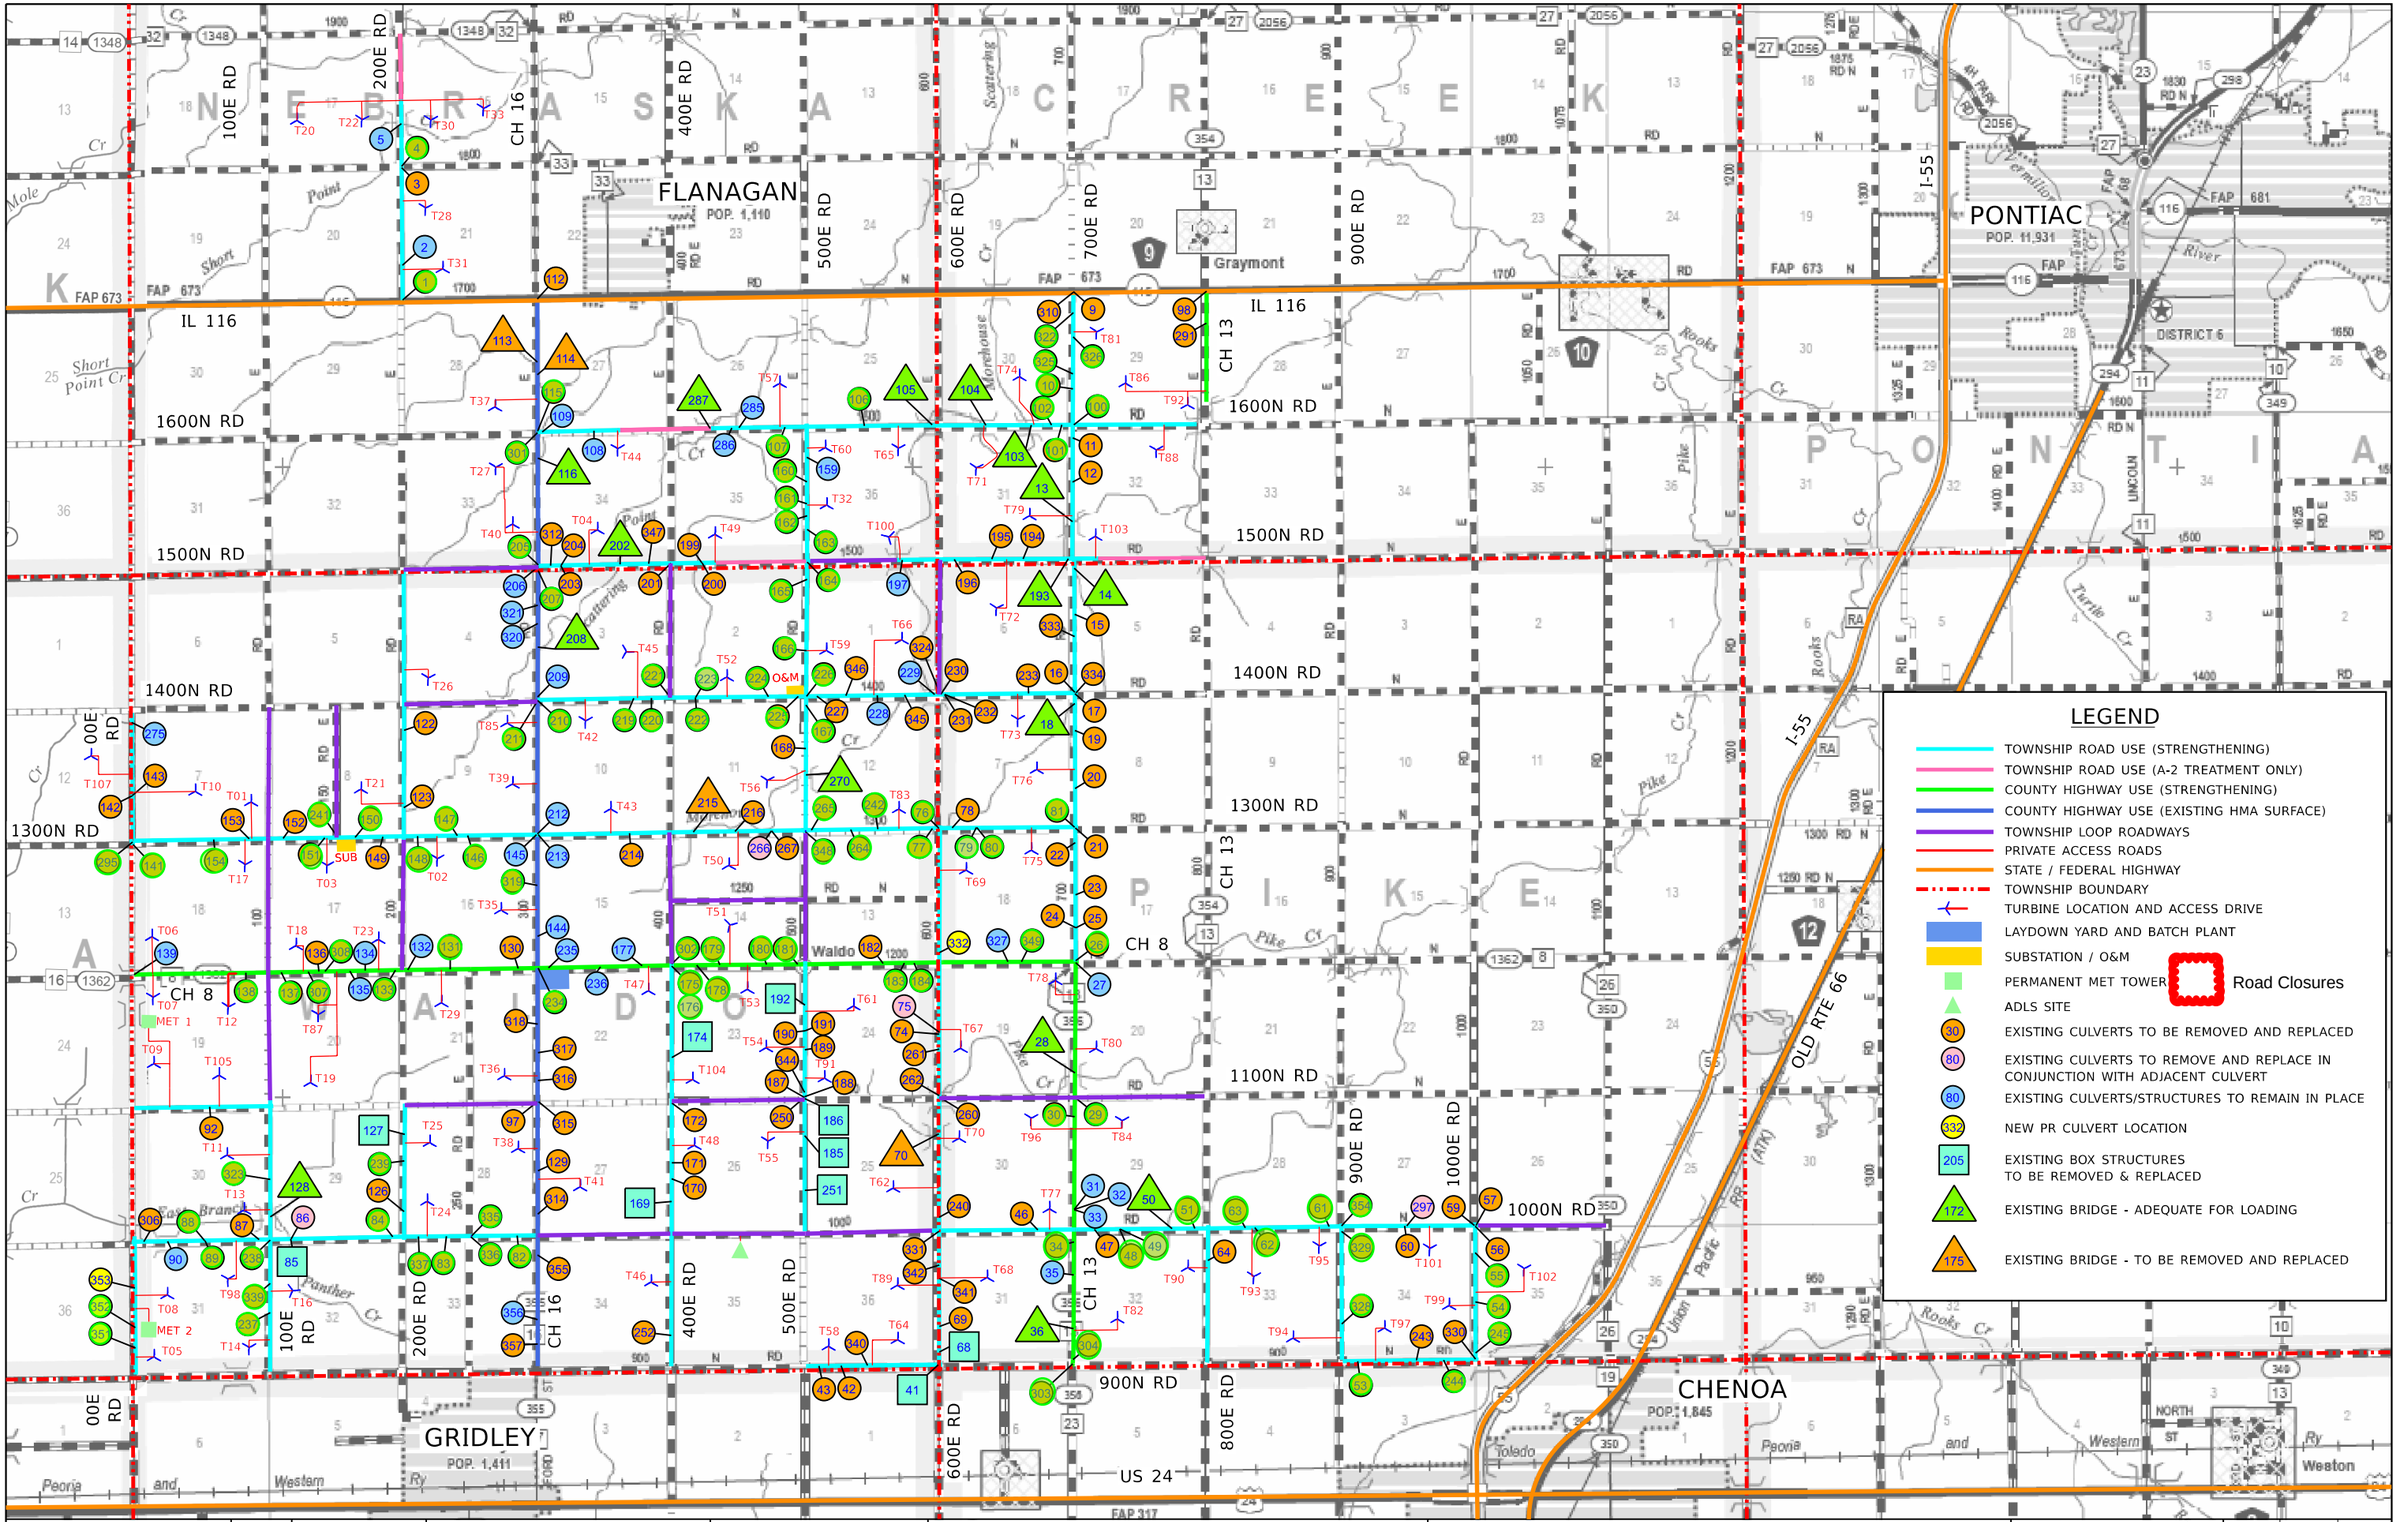

REV	DATE	DESCRIPTION
1	4/10/2026	REV 1
00	2/20/2026	IFC SUBMITTAL

DESIGNED - JDA
DRAWN - DRR/LNS
CHECKED - ML
DATE - 04/14/2026

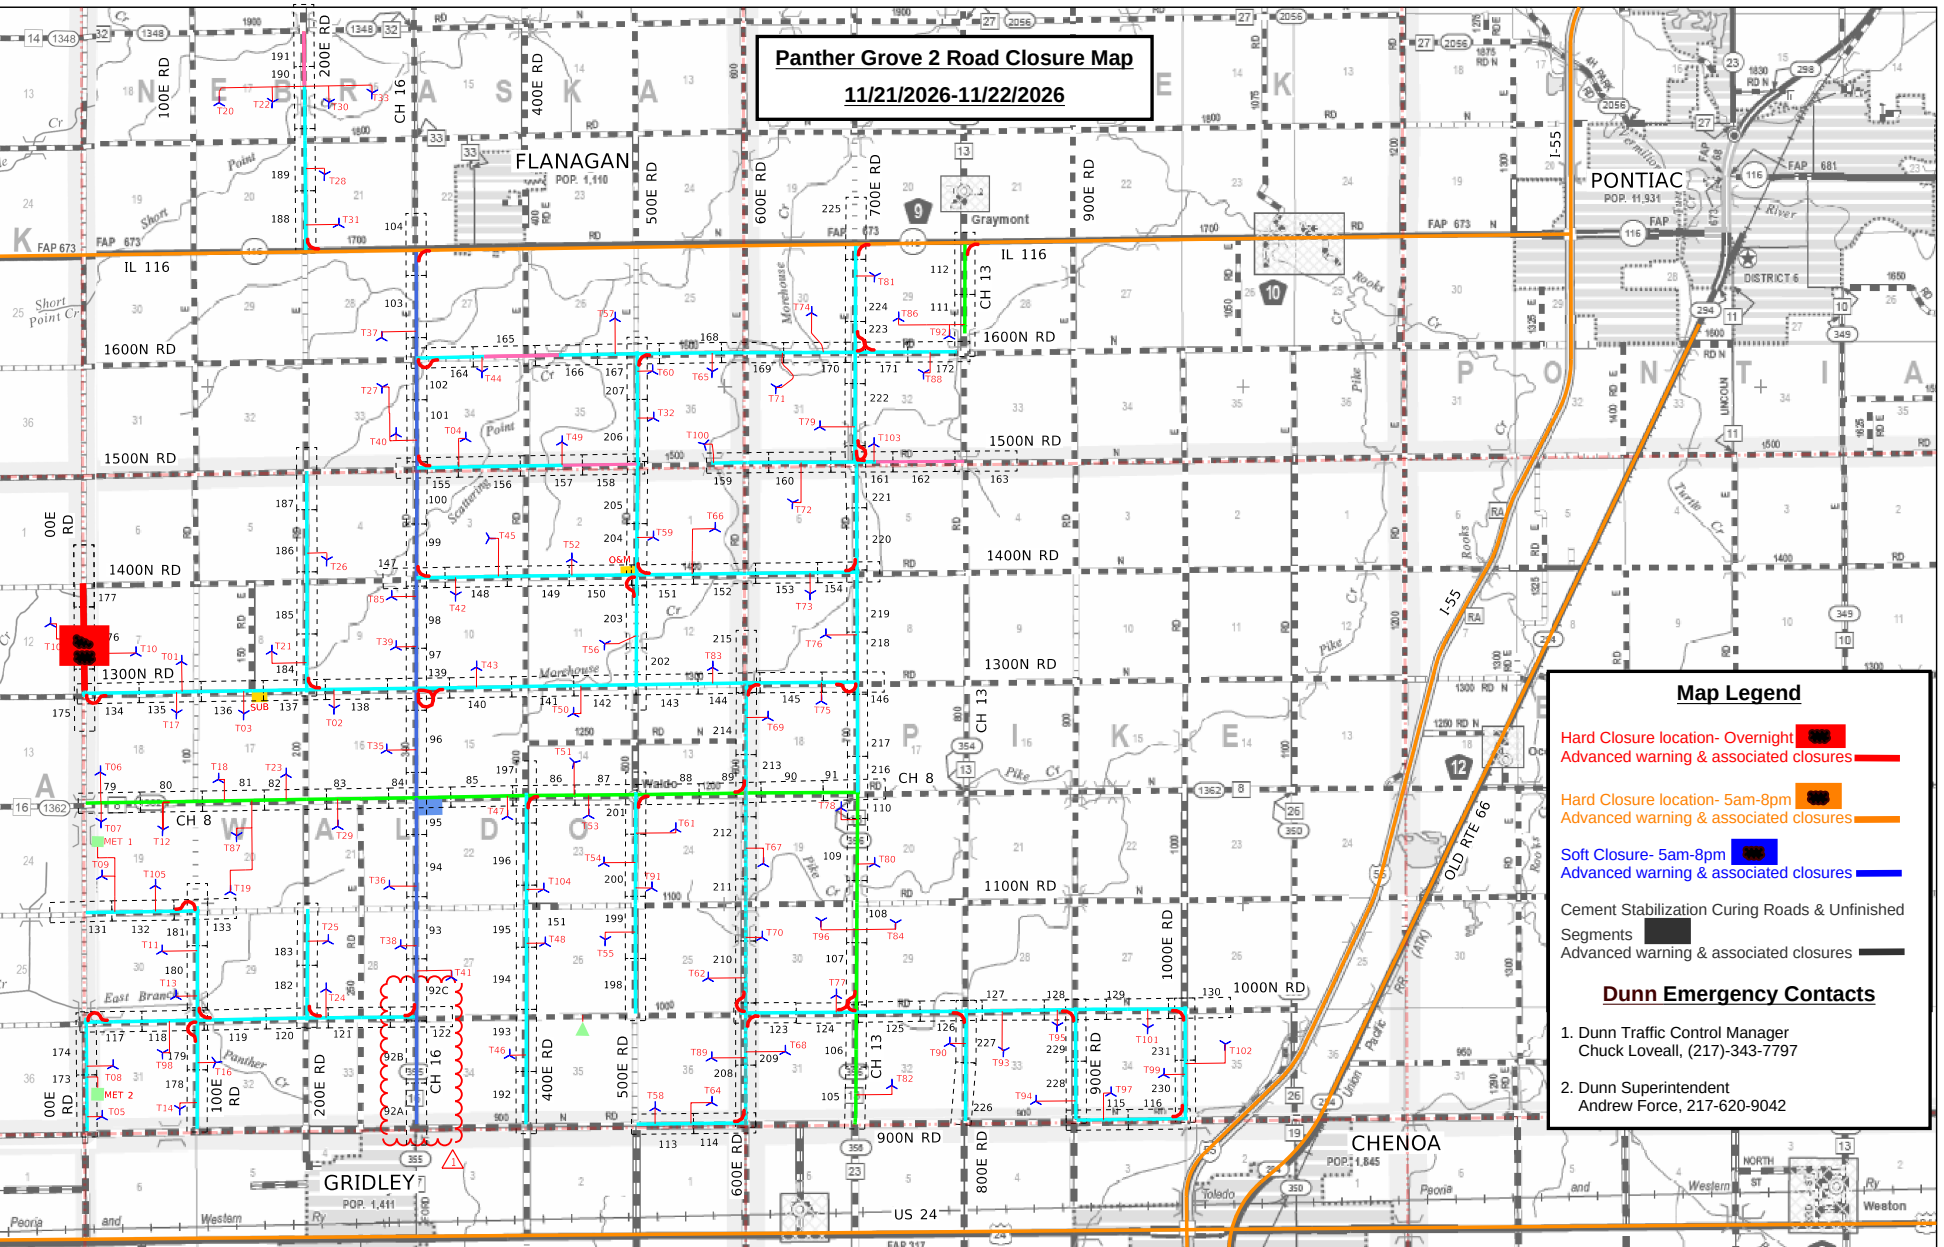
PANTHER GROVE 2 WIND PROJECT
LIVINGSTON COUNTY, ILLINOIS

EXHIBIT A – PROJECT LAYOUT MAP (REVISION 1)

SCALE: N.T.S. | SHEET 1 OF 1 SHEETS | STA. | TO STA.

Farnsworth GROUP
100 WALNUT ST #200
PEORIA, ILLINOIS 61602
(309) 689-9888 / Info@f-w.com

TOTAL SHEETS	SHEET NO.	REVISION NO.


Panther Grove 2 Road Closure Map
11/21/2026-11/22/2026
FLANAGAN
POP. 1,110
PONTIAC
POP. 11,931
GRIDLEY
POP. 1,411
CHENOA
POP. 1,845
Graymont
IL 116
1600N RD
1500N RD
1400N RD
1300N RD
1100N RD
1000N RD
900N RD
100E RD
200E RD
400E RD
500E RD
600E RD
700E RD
800E RD
900E RD
CH 16
CH 13
CH 8
I-55
US 24
OLD RTE 66
Map Legend
Hard Closure location- Overnight
Advanced warning & associated closures
Hard Closure location- 5am-8pm
Advanced warning & associated closures
Soft Closure- 5am-8pm
Advanced warning & associated closures
Cement Stabilization Curing Roads & Unfinished Segments
Advanced warning & associated closures
Dunn Emergency Contacts
1. Dunn Traffic Control Manager
Chuck Loveall, (217)-343-7797
2. Dunn Superintendent
Andrew Force, 217-620-9042
