Panther Grove 2

	4-Nov-26	Today
Daily Weather as of 7:00am	Cloudy	Cloudy
Low Temperature (F)	51	47
High Temperature (F)	66	66
Ground Wind Speed (MPH):	15mph	12 mph
Precipitation (in)	0.30	7%
November Precip Total (In)	0.30	

Daily Safety Topics

Headlights/Taillights: When doing daily inspections make sure your headlights and taillights are visible. Take the time to wipe any mud or dirt off them to allow them to be seen from a distance. And report any lighting issues so they can be replaced or repaired.

Ergonomics- fitting the job to the worker, rather than forcing the body to adapt to an uncomfortable or unsafe task.

Site Notes

Thursday, November 5, 2026

	ACTIVITY	LAST WORKING DAY Wednesday, November 4, 2026 LOCATION(S)	TODAY Thursday, November 5, 2026 LOCATION(S)	NEXT WORKING DAY Friday, November 6, 2026 LOCATION(S)
Public Roads	Strip Public Road Radii			
	Mowing Public Road Radii			
	Stone Public Road Radii	P11 (1400N RD / CH 16)		
Access Roads	Strip Access Road			
	Cement Stabilization			
	Stone Access Road			
	Strip Access Road Radii			
	Stone Access Road Radii			

Quantity Tracking

QTY LAST WORKDAY	QTY TO DATE	UNIT	TOTAL QTY	% COMPLETE
	11	EA	35	31.4%
	9	EA	35	25.7%
	66695	LF	161120	41.4%
	67827.5	LF	161120	42.1%
	55073.5	LF	161120	34.2%
	63	EA	TBD	#VALUE!
	59	EA	TBD	#VALUE!

Site Information

Manpower	
19	White Construction Management
47	White Construction Operators
27	White Construction Laborers
16	White Construction Ironworkers
0	White Construction Millwright
3	White Construction Electrician
40	Dunn Company
8	West Wind
4	Tobey's Construction & Cartage
8	KVCC
6	Prairie Materials
19	JF Edwards
5	Keeley
202	**Total**

Equipment	
48	Pickup Trucks
3	Dozers
0	Rollers
1	Graders
1	Cargo Trailer
0	Cranes
3	Excavators
0	Forklift
13	Trailers
0	Sand Truck
1	Sheepfoot Roller
0	Reclaimer Stabilizer
1	Smooth Drum Roller
2	Water Trucks
5	Skid Steer
78	**Total**

Additional Comments

Plan of the Day (POD) Report

5-Nov-2026

PANTHER GROVE WIND ENERGY FACILITY

Weather Notes: Rain out on 10-15	LAST WORKING DAY	TODAY	NEXT WORKING DAY	2-Day Lookahead
	65° / 49° Temp Range	50° / 41° Temp Range	48° / 38° Temp Range	49° / 35° Temp Range
	81% | 0.04 in | 12 AM - 8 AM Precipitation	39% | 0.02 in | 5 PM - 9 PM Precipitation	10% | 0.00 in | None Precipitation	None Precipitation
	None | None Lighting Risk	None | None Lighting Risk	None | None Lighting Risk	None | None Lighting Risk
	None | 0% | None Severe Forcast	None | 0% | None Severe Forcast	None | 0% | None Severe Forcast	None | 0% | None Severe Forcast
	21.3 Max Wind	17 Max Wind	16 Max Wind	8.4 Max Wind
	38.9 Max Gust	30 Max Gust	28.9 Max Gust	13.9 Max Gust
(S) Start (C) Continue (F) Finish	Wednesday, November 4, 2026	Thursday, November 5, 2026	Friday, November 6, 2026	Saturday, November 7, 2026

Today's Notes

Active Cure	Date	Day	Cure		
CH8:CH16-400E	10/23	13	10/30		
N/A					
N/A					
N/A					
N/A					

Manpower	Scope	QTY
Dunn Company	Agg Surface, Earthwork	15
Tobey's Constr.	Pipe Culvert	0
KVCC	Agg Surface	0
Millennia	QC	0
Material Serv. Test.	QC	0
Beniach	Oil and Chip	0

Notes:

Box Culvert: In procurement

Pipe Culvert: Ongoing

Agg Widening: On hold

Profile Adj./Add Rock: On hold

Pulverization: on hold

Stabilization: on hold

Agg Surface: on hold

Oil and Chip: on hold

Earthwork: Using existing material where possible, brining new to locations as needed. Roads listed in punchwork section.


Seeding: Resuming this week

HMA: On hold until IDOT permits are in place.

Punchlist: On going

	LAST WORKING DAY		TODAY		NEXT WORKING DAY		2-Day Lookahead	
	LOCATION(S)		LOCATION(S)		LOCATION(S)		LOCATION(S)	
	Road	Repening	Road	Repening	Road	Repening	Road	Repening
Long Duration Road Closures	☐ CH13:900N-1000N	11/2/2026	☐ CH13:900N-1000N	11/2/2026	☐ CH13:900N-1000N	11/2/2026	☐ CH13:900N-1000N	11/2/2026
	☐ CH13:1000N-1100N	11/2/2026	☐ CH13:1000N-1100N	11/2/2026	☐ CH13:1000N-1100N	11/2/2026	☐ CH13:1000N-1100N	11/2/2026
	☐ CH13:1100N-CH8	11/2/2026	☐ CH13:1100N-CH8	11/2/2026	☐ CH13:1100N-CH8	11/2/2026	☐ CH13:1100N-CH8	11/2/2026
	☐ CH8:CH13-600E	11/2/2026	☐ CH8:CH13-600E	11/2/2026	☐ CH8:CH13-600E	11/2/2026	☐ CH8:CH13-600E	11/2/2026
	☐ CH8:CH13-800E	11/2/2026	☐ CH8:CH13-800E	11/2/2026	☐ CH8:CH13-800E	11/2/2026	☐ CH8:CH13-800E	11/2/2026
	☐ 700E:CH8-1300N	11/2/2026	☐ 700E:CH8-1300N	11/2/2026	☐ 700E:CH8-1300N	11/2/2026	☐ 700E:CH8-1300N	11/2/2026
	☐ CH8:600E-500E	11/2/2026	☐ CH8:600E-500E	11/2/2026	☐ CH8:600E-500E	11/2/2026	☐ CH8:600E-500E	11/2/2026
	☐ CH8:CH16-400E	11/2/2026	☐ CH8:CH16-400E	11/2/2026	☐ CH8:CH16-400E	11/2/2026	☐ CH8:CH16-400E	11/2/2026
Short Duration Road Closures	☑ 900N:900E-1000E	11/4/2026	☑ 1000E:900N-1000N	11/5/2026				
	☑ 900N:1000E-1100E	11/4/2026						
	☑ 1000E:900N-1000N	11/4/2026						

Public Road Improvements		QTY Last Work Day	QTY Complete	Unit	Total QTY	% Complete				
	Box Culvert		0.0	1.0	EA	15.0	6.7%			
	Pipe Culvert	F 245	1.0	108.0	EA	222.0	48.6%	S 54 S 55		
	Aggregate Widening	Trenching Aggregate Install-Trench Fill	0.0 0.0	23.0	Mi	75.0	30.7%	Trenching Aggregate Install-Trench Fill	Trenching Aggregate Install-Trench Fill	Trenching Aggregate Install-Trench Fill
	Prof. Adj.		0.0	12.0	EA					
	Pulverization		0.0	23.5	Mi	75.0	31.3%			
	Stabilization		0.0	23.5	Mi	75.0	31.3%			
	Agg Surface		0.0	23.5	Mi	75.0	31.3%			
	Oil and Chip		0.0	23.5	Mi	75.0	31.3%	S CH8:CH16-400E		
	Earthwork		0.0	23.5	Mi	75.0	31.3%			
	Seeding		0.0	23.5	Mi	75.0	31.3%			
	Punchlist		0.0	23.5	Mi	75.0	31.3%			
	HMA	S CH 8 Patches	0.0	7.0	EA	17.0	41.2%	C CH 8 Patches	CH 16 Patches 113	
Site	Crane Pad			12.0	EA	109.0	11.0%			
	Access Road		0.0	40.0	EA	109.0	36.7%			

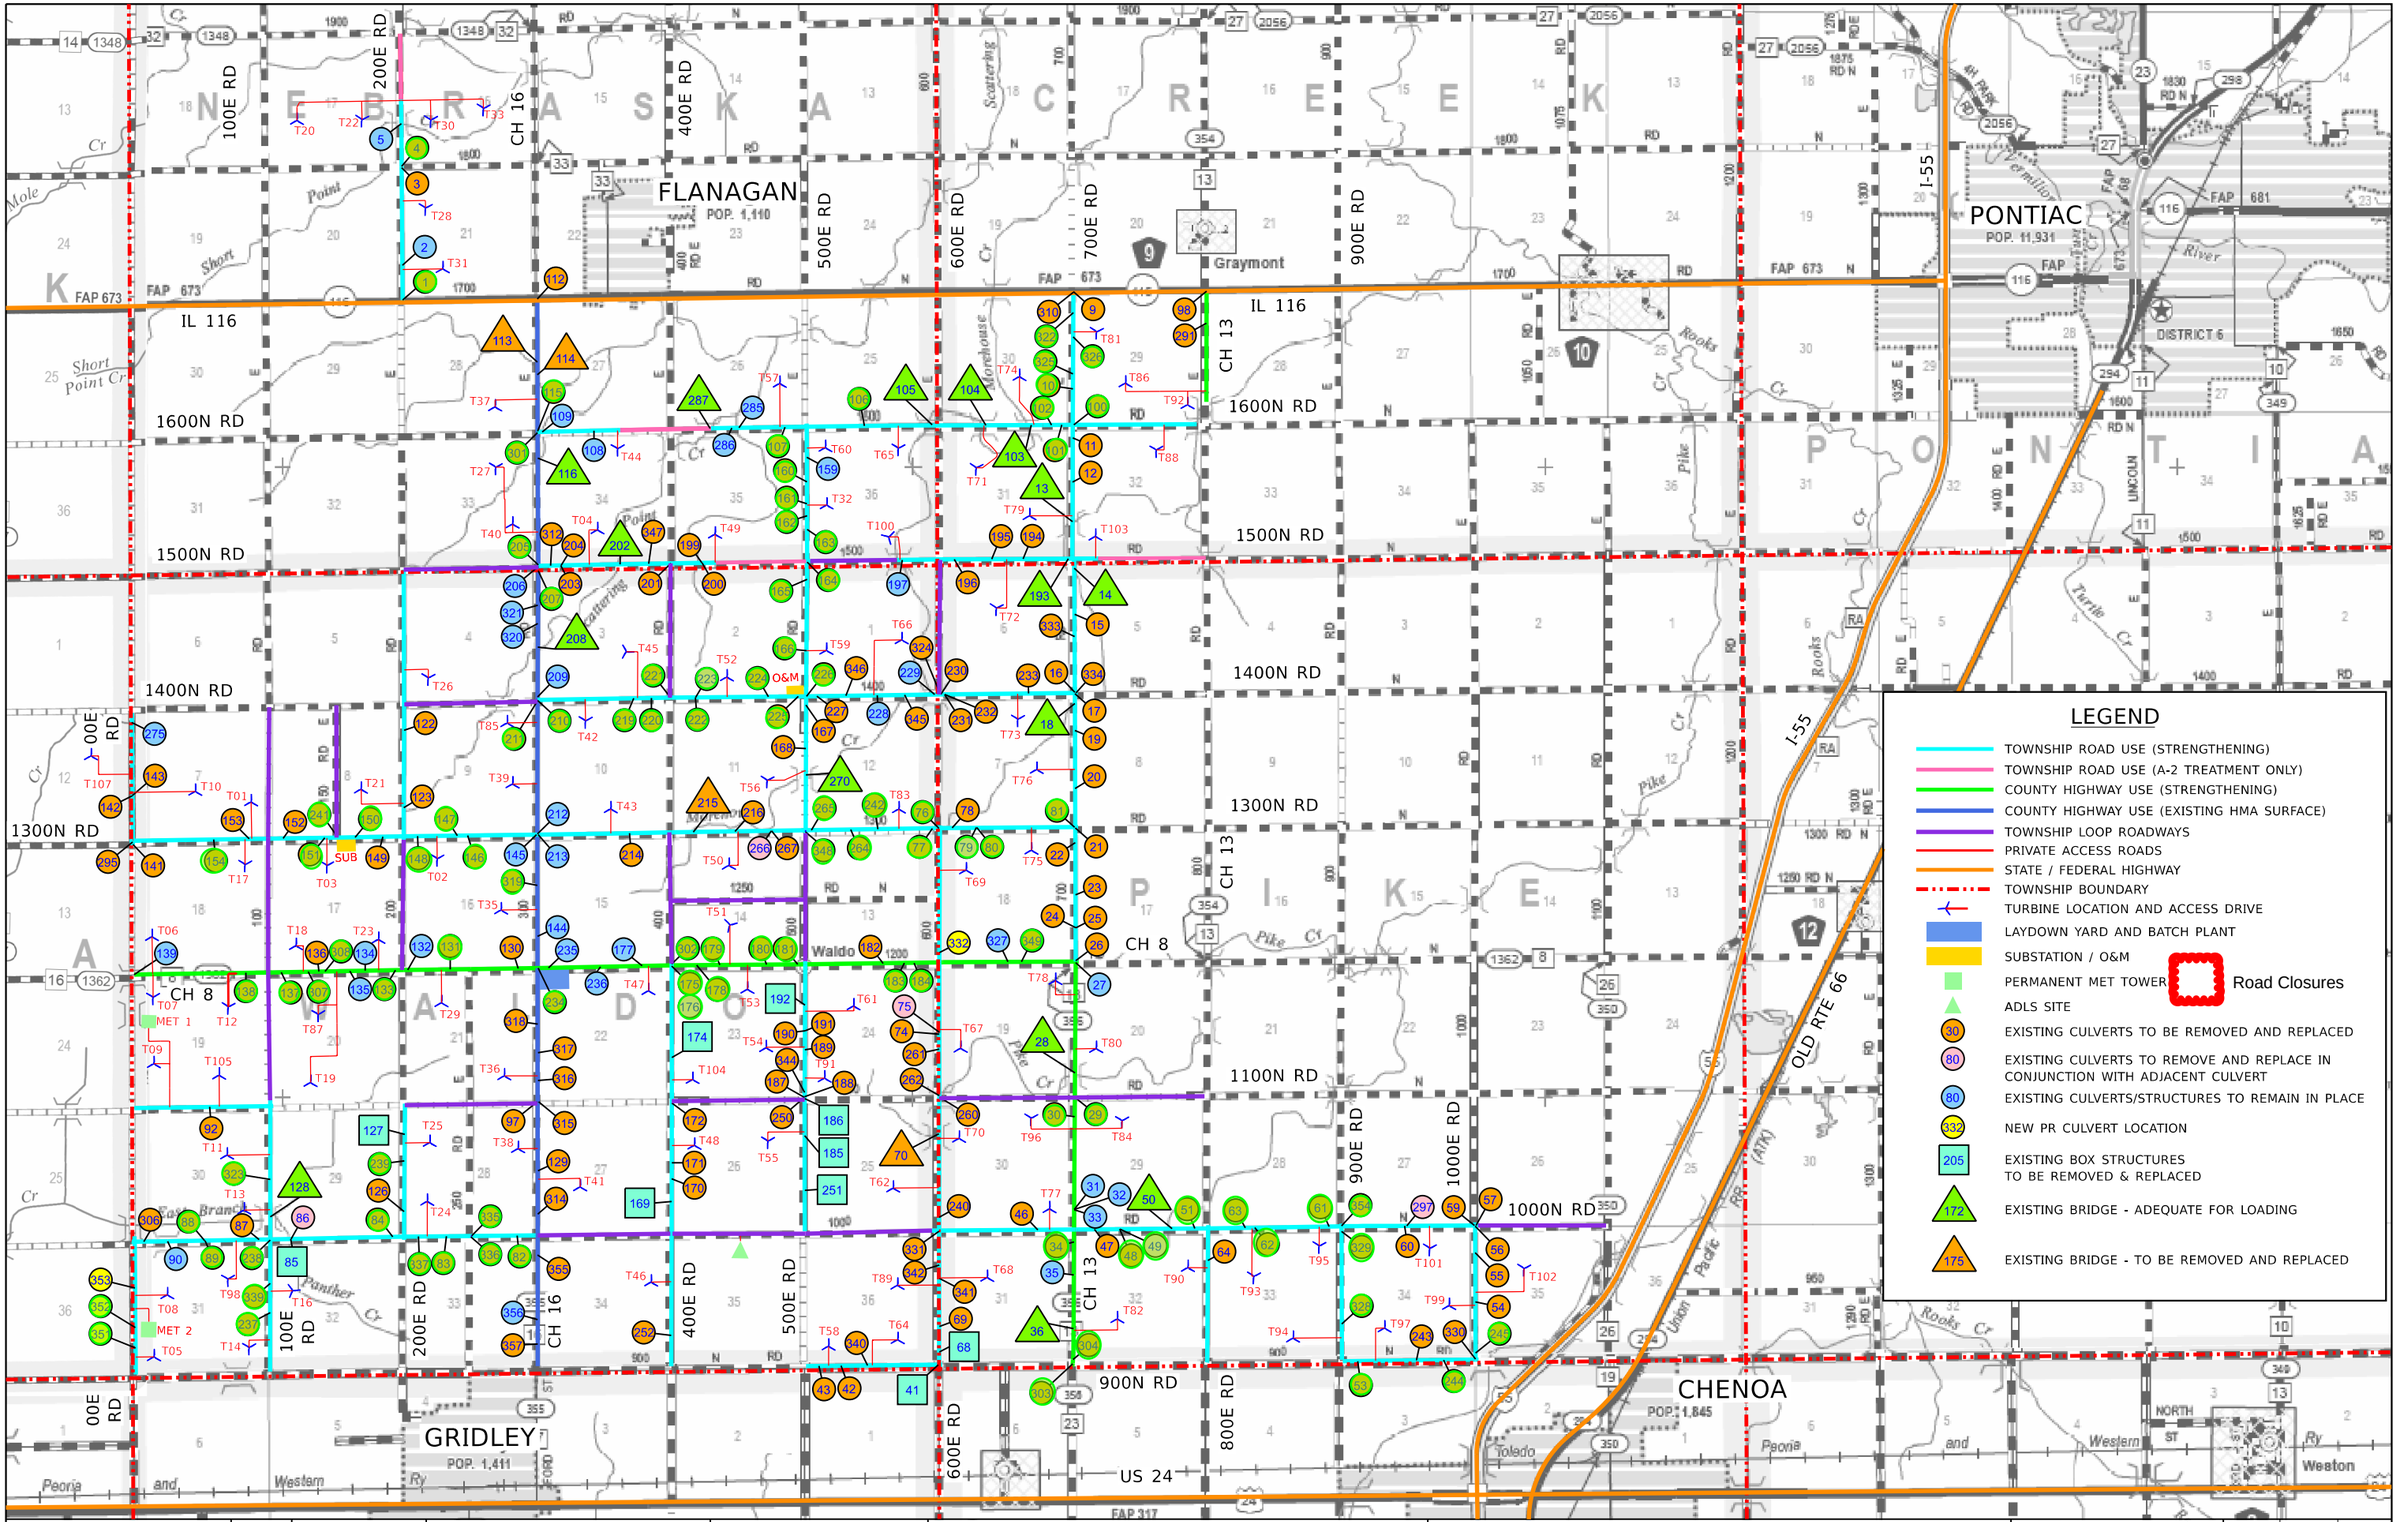

REV	DATE	DESCRIPTION
1	4/10/2026	REV 1
00	2/20/2026	IFC SUBMITTAL

DESIGNED - JDA
DRAWN - DRR/LNS
CHECKED - ML
DATE - 04/14/2026

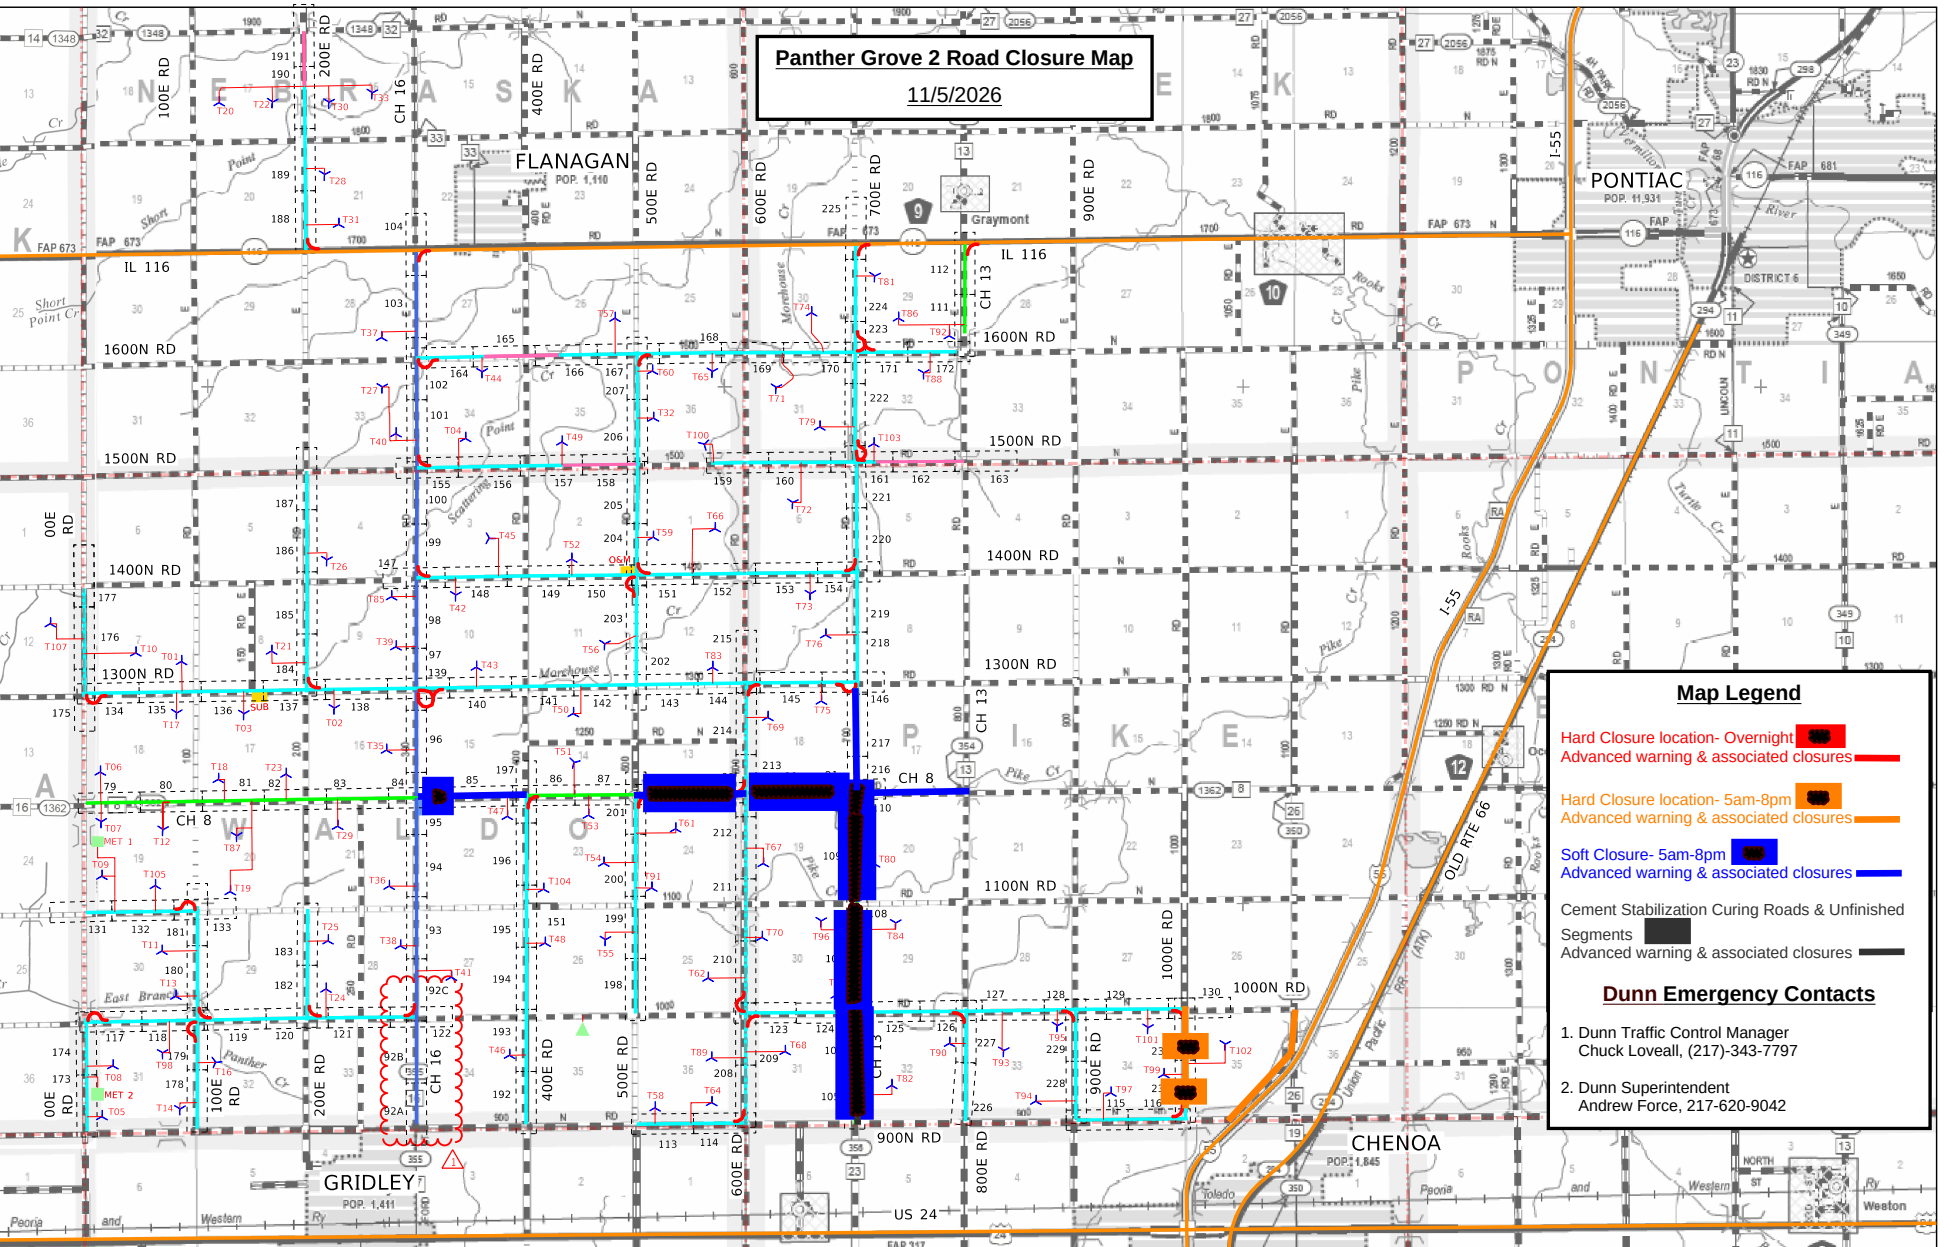
PANTHER GROVE 2 WIND PROJECT
LIVINGSTON COUNTY, ILLINOIS

EXHIBIT A – PROJECT LAYOUT MAP (REVISION 1)

SCALE: N.T.S. | SHEET 1 OF 1 SHEETS | STA. TO STA.

Farnsworth GROUP
100 WALNUT ST #200
PEORIA, ILLINOIS 61602
(309) 689-9888 / Info@f-w.com

TOTAL SHEETS	SHEET NO.	REVISION NO.


Panther Grove 2 Road Closure Map
11/5/2026
Map Legend
Hard Closure location- Overnight
Advanced warning & associated closures
Hard Closure location- 5am-8pm
Advanced warning & associated closures
Soft Closure- 5am-8pm
Advanced warning & associated closures
Cement Stabilization Curing Roads & Unfinished Segments
Advanced warning & associated closures
Dunn Emergency Contacts
1. Dunn Traffic Control Manager
Chuck Loveall, (217)-343-7797
2. Dunn Superintendent
Andrew Force, 217-620-9042
FLANAGAN
POP. 1,110
PONTIAC
POP. 11,931
GRIDLEY
POP. 1,411
CHENOA
POP. 1,845
IL 116
1600N RD
1500N RD
1400N RD
1300N RD
1100N RD
1000N RD
900N RD
CH 8
CH 13
CH 16
I-55
US 24
OLD RTE 66
100E RD
200E RD
400E RD
500E RD
600E RD
700E RD
800E RD
900E RD
1000E RD
